


PROJECT FACT SHEET
February 6, 2007

PROJECT: Rouge River Oxbow, Wayne Co., MI

DESCRIPTION: The purpose of the project is the reconnection of the Rouge River Oxbow segment to the main Rouge River channel at Greenfield Village, located in Dearborn, Michigan, by construction of inlet and outlet openings. During the mid-1970s, Corps flood control efforts channelized the river, cutting off the oxbow and eliminating flood plain wetlands and habitat.

CONGRESSIONAL INTEREST: Cheeks-Kilpatrick (D) MI-13; Dingell (D) MI-15; Senator Carl Levin (D) MI

LOCATION MAP & PICTURE:

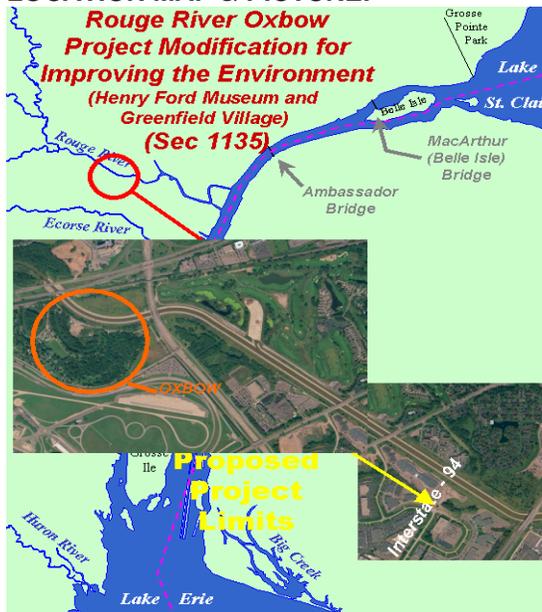

NON-FEDERAL PROJECT SPONSOR: The Henry Ford. POC is Steven K. Hamp, President, (313) 271-1620

PROJECT AUTHORITY: Section 1135(b) of the Water Resources Development Act of 1986, as amended.

FUNDING:

	<u>Total</u>	<u>Federal</u>	<u>Non-Federal</u>
Current Working Estimate	\$ 6,855,000	\$ 4,461,000	\$ 2,394,000
Funds allocated prior to FY07	\$ 133,172	\$ 133,172	\$ 0
Funds allocated in FY07	\$ 0	\$ 0	\$ 0
FY08 Budget	\$ 0	\$ 0	\$ 0
Funds that could be used in FY08	\$ 200,000	\$ 100,000	\$ 100,000
Funds required to complete (> FY08)	\$ 6,721,828	\$ 4,327,828	\$ 2,394,000

STAGE: Feasibility

STATUS: This proposal for the reconnection of the oxbow to the river is Phase 3 of the oxbow recovery. Phase 1 was the restoration of the oxbow habitat, and Phase 2 was the relocation of a CSO in the study area, both completed without Corps participation. The Feasibility Stage is being continued with FY2008 funds. Downstream opening is to be by private venture. The upstream opening will be part of the USACE project. The Detailed Project Report (DPR) is to be completed in Sep 2007. Plans and Specifications can be initiated in FY2008.

PM: Pat Kuhne, 313-226-6767, patrick.a.kuhne@lre02.usace.army.mil
